



P.O. Box 667 • 118 North Main Street • Goddard, Kansas 67052 • ph 316-794-2441 • fax 316-794-2401

To: Honorable Mayor and City Council  
 From: Brian W. Silcott, City Administrator  
 Cc: Department Directors & Staff  
 Re: City Administrator Report for the week of August 3, 2020  
 Date: August 3, 2020

Below is a brief update on City operations, projects, and future agenda items for the City. The next City Council meeting is scheduled for Monday, August 17, 2020. City Administrator reports can be found online on the City webpage for City Administration reports from 2008 to present. ([CLICK HERE](#))

**STAR Bond:** Construction of the aquatic center/natatorium continues to make significant progress the construction of the pool roof trusses is complete, and installation of the rooftop is ongoing. After the roof is constructed work on the interior will begin. Further dirt work around the site has also increased in the last two weeks. The open area at the top left-hand side is the aquatic park, which is privately funded and beyond the scope of the City's participation in the project. The picture on the right is looking east at the dirt work for the health club. Almost the entirety of the interior work requires preorder processing. Below is a list of STAR Bond project funds and updated pictures of the development. There have been no new project fund distributions since March.

Disbursement #	Date	Amount	Developer	Total to Developer
1	09.29.2014	\$ 2,907,966.48	Goddard Destination	\$ 2,907,966.48
2	11.20.2018	\$ 2,131,225.20	Goddard Sports	
3	02.08.2019	\$ 2,552,466.60		
4	04.17.2019	\$ 1,914,790.50		
5	06.06.2019	\$ 2,290,951.80		
6	08.09.2019	\$ 1,839,832.20		
7	10.29.2019	\$ 1,910,912.40		
8	12.20.2019	\$ 2,034,346.14		
9	02.24.2020	\$ 1,791,610.20		
10	03.31.2020	\$ 2,045,210.40		
11	05.20.2020	\$ 1,524,619.26		
12	07.20.2020	\$ 1,230,108.14		
				\$ 21,266,072.84
TOTAL		\$ 24,174,039.32	Tie Line	\$ 24,174,039.32
			\$ -	
	Project Accounty Fund Initial Deposit	\$ 25,400,000.00	% Remaining	% Expended
	Project Balance:	\$ 1,225,960.68	4.83%	95.17%



Arbor Creek Addition: Work continues to on Phase 1 of this this addition, which includes 55 homes, sanitary sewer mains & laterals, and paving the middle of the subdivision's club house. Total special assessments for this phase is \$2,891,000. The estimated average home value of this addition is \$300,000 each home generating approximately \$1,150 in municipal property tax with Phase 1 generating an estimated \$63,250 annually and \$281,750 annually at full build out. Arbor Creek has 245 lots with 12 lots already sold with 43 phase 1 lots and 233 total lots remaining. The project has issued \$2,939,300 in temporary notes having paid \$1,267,691.08.




Clover Leaf Addition: Work on the water, sanitary sewer, and stormwater is complete, and the installation of paving is underway. Clover Leaf contains 133 total lots. Phase 1 consists of 50 total homes with 22 lots sited along Martens Ct. for duplex units which will increase water and sewer customer count by 44 users. Phase 1 also includes 28 lots for single family residential homes. Clover Leaf Phase 1 has \$2,211,000 in special assessments. Below is an updated picture of the dirt work and recent paving completed for the development. Clover Leaf has \$2,211,000 issued with A-1 rated (AAA equivalent) special temp notes issued and \$1,427,819.33 paid.



RCUT Project: KDOT has completed its preliminary field plan review. The City Engineer and staff is meeting with TranSystems late this week to review the changes. The project continues to be on pace for a September 24, 2020 bid letting. The approved design budget is \$186,210 with \$59,085.97 being expensed to date. The estimated total cost of construction is \$1,810,000 with KDOT covering the cost of construction. This is project # 2020-01 and KDOT Project #54-87 KA-4362-01.



183<sup>rd</sup> Street Frontage & Intersection: Thanks to the assistance and shepherding of the City Engineer and his team at Certified Engineering Design, we've submitted a request for funding for the intersection improvement at 183<sup>rd</sup> Street West & US-54/400/Kellogg. On June 9<sup>th</sup> we submitted the request to advertise for bids on the Kellogg Drive Relocation Project (KDOT Project #87 KA-5215-01). The notice to proceed with the solicitation of bids is anticipated any day. The approved construction budget is \$656,000 with KDOT covering the cost of construction. This is project # 2020-02 and KDOT Project #87 KA-5215-01.

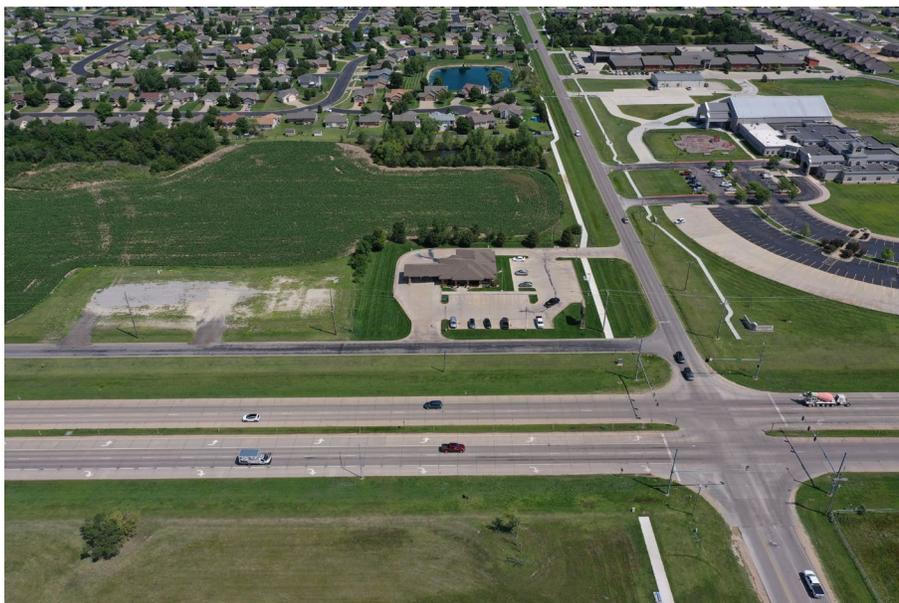

**2<sup>nd</sup> Street Project:** The project was approved at the July 6th meeting and was completed the week of July 27<sup>th</sup>. The project budget is \$16,234 allocated to the Street Fund's annual Street Maintenance Program (40-410-8410). As discussed at the July 6th meeting and during the CIP discussion, upon completion the City Engineer & Public Works Director will assess the repair and if successful and approved by the City Council will be applied to the remaining unpaved streets as part of the 2020 road maintenance program. If unsuccessful, staff will present additional options in the autumn as part of the 2020 street maintenance program.



**119<sup>th</sup> Street Water Valve:** The water valve installation that was approved at the July 6th meeting and was found to have a non-standard size valve that required a special order briefly delaying the project has been completed. The 8" water valve cost totaled \$6,630.00 and is being allocated to line item 82-620-6150



CDBG COVID Grant: The City's application for the Small Cities Community Development Block Grant (CDBG) Corona Virus Supplement Program funding has been approved for \$132,000. City staff will be reaching out to local businesses over the next several weeks to receive applications for the distribution of funds. Fund distribution must be completed by September 20, 2020 as the unspent funds will be returned to HUD after that date.

St. Andrews 4<sup>th</sup> Addition Assessment Bonds: Staff will present a bond sale resolution at the August 17th City Council meeting. This resolution will authorize the solicitation of bids for the 20-year General Obligation Bonds. The final action of the City Council on this item will occur at the Tuesday, September 8th City Council meeting where another bond resolution and bond ordinance will be considered to accept the best bid (due at 1100) and finalize the sale of the bonds.

Respectfully Submitted,  
Brian W. Silcott,

A handwritten signature in blue ink that reads "Brian W. Silcott". The signature is written in a cursive style with a stylized "S" at the end.

City Administrator
